


## ***Appendix A: Initial Project Schedule***


---



█ Actual Work     █ Critical Remaining Work     ▶ Summary  
█ Remaining Work     ◆ Milestone

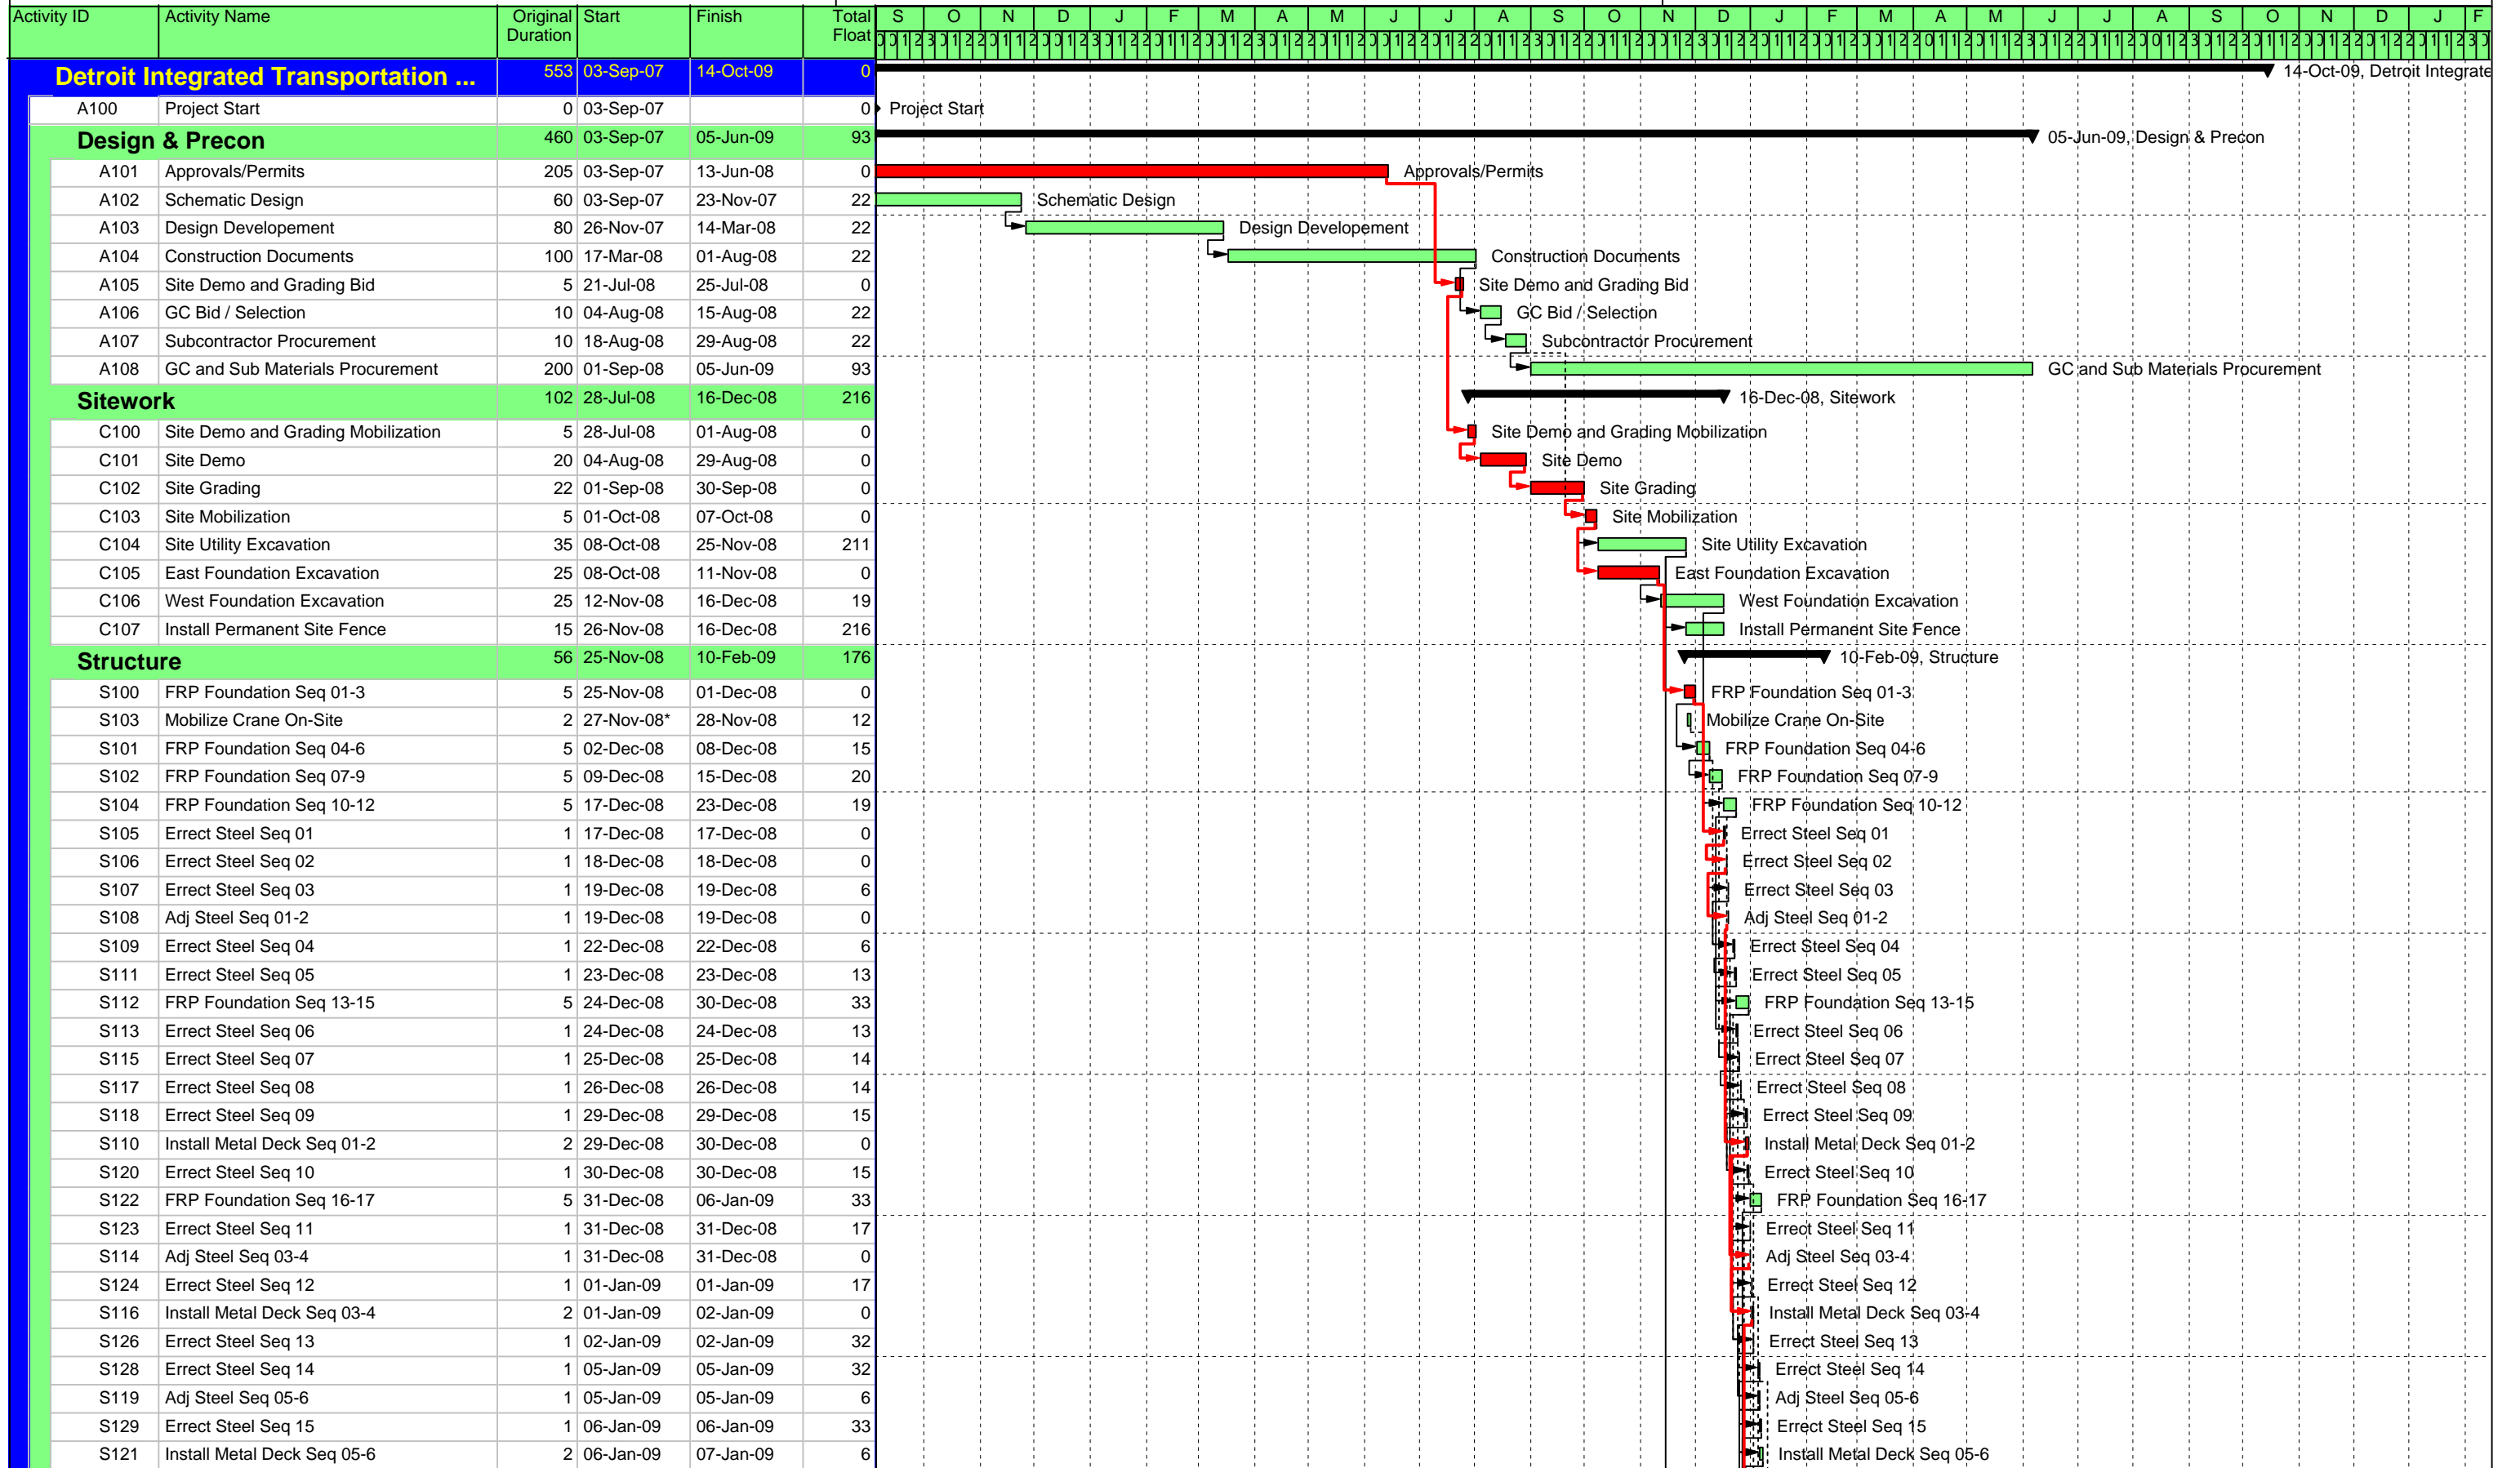

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
F116	Install Metal Panels Seq 10-12	8	27-Feb-09	10-Mar-09	1
F122	Aluminum Windows Seq 7-9	4	27-Feb-09	04-Mar-09	10
F115	Brick Masonry Seq 16-17	16	04-Mar-09	25-Mar-09	0
F118	Roof Insulation & Membrane Seq 13-15	8	09-Mar-09	18-Mar-09	142
F120	Install Metal Panels Seq 13-15	5	11-Mar-09	17-Mar-09	1
F124	Aluminum Windows & Ext. Doors Seq 1...	4	11-Mar-09	16-Mar-09	6
F123	Install Metal Panels Seq 16-17	5	18-Mar-09	24-Mar-09	1
F125	Aluminum Windows Seq 13-15	1	18-Mar-09	18-Mar-09	5
F121	Roof Insulation & Membrane Seq 16-17	8	19-Mar-09	30-Mar-09	142
F126	Aluminum Windows & Ext. Doors Seq 1...	2	26-Mar-09	27-Mar-09	0
F127	Building Enclosure	0	27-Mar-09	27-Mar-09	0
<b>Site Paving &amp; Landscape</b>		<b>55</b>	<b>30-Mar-09</b>	<b>12-Jun-09</b>	<b>88</b>
C108	Site Paving	15	30-Mar-09	17-Apr-09	88
C109	Site Concrete	20	20-Apr-09	15-May-09	88
C110	Landscaping	20	18-May-09	12-Jun-09	88
<b>Interiors</b>		<b>152</b>	<b>22-Jan-09</b>	<b>21-Aug-09</b>	<b>38</b>
I100	Elevator Shaft Wall	12	22-Jan-09	06-Feb-09	158
I101	Elevator Rail & Cab Installation	20	09-Feb-09	06-Mar-09	158
<b>Level 2 Interiors</b>		<b>134</b>	<b>22-Jan-09</b>	<b>28-Jul-09</b>	<b>56</b>
I102	Boiler Room Mechanical	15	22-Jan-09	11-Feb-09	175
I103	Ductwork Mains Lev 2 Seq 01-6	7	03-Feb-09	11-Feb-09	8
I104	Ductwork Mains Lev 2 Seq 07-11	10	12-Feb-09	25-Feb-09	24
I106	Interior Metal Studs Lev 2 Seq 01-6	6	25-Feb-09	04-Mar-09	8
I105	Ductwork Mains Lev 2 Seq 12-17	6	27-Feb-09	06-Mar-09	30
I107	Interior Metal Studs Lev 2 Seq 07-11	9	05-Mar-09	17-Mar-09	19
I108	MEP Rough-In Lev 2 Seq 01-6	6	10-Mar-09	17-Mar-09	8
I109	Interior Metal Studs Lev 2 Seq 12-17	6	18-Mar-09	25-Mar-09	28
I110	MEP Rough-In Lev 2 Seq 07-11	9	18-Mar-09	30-Mar-09	19
I112	Drywall Lev 2 Seq 01-6	9	30-Mar-09	09-Apr-09	0
I111	MEP Rough-In Lev 2 Seq 12-17	6	31-Mar-09	07-Apr-09	25
I113	Drywall Lev 2 Seq 07-11	12	10-Apr-09	27-Apr-09	11
I115	Drywall Lev 2 Seq 12-17	9	28-Apr-09	08-May-09	11
I114	Paint Lev 2 Seq 01-6	6	01-May-09	08-May-09	0
I116	Paint Lev 2 Seq 07-11	9	11-May-09	21-May-09	11
I118	Paint Lev 2 Seq 12-17	6	22-May-09	29-May-09	11
I117	Ceiling Grid Lev 2 Seq 01-6	5	26-May-09	01-Jun-09	0
I119	Ceiling Grid Lev 2 Seq 07-11	5	02-Jun-09	08-Jun-09	7
I120	Light Fixtures & GRDs Lev 2 Seq 01-6	5	02-Jun-09	08-Jun-09	0
I121	Ceiling Grid Lev 2 Seq 12-17	5	09-Jun-09	15-Jun-09	8
I122	Light Fixtures & GRDs Lev 2 Seq 07-11	5	09-Jun-09	15-Jun-09	7
I123	Millwork Lev 2 Seq 01-6	6	09-Jun-09	16-Jun-09	0
I124	Light Fixtures & GRDs Lev 2 Seq 12-17	5	16-Jun-09	22-Jun-09	8
I125	Millwork Lev 2 Seq 07-11	6	17-Jun-09	24-Jun-09	6
I126	Millwork Lev 2 Seq 12-17	6	25-Jun-09	02-Jul-09	6
I127	Hang Doors Lev 2 Seq 01-6	3	30-Jun-09	02-Jul-09	0
I128	Hang Doors Lev 2 Seq 07-11	6	03-Jul-09	10-Jul-09	0
I129	Floor Finishes Lev 2 Seq 01-6	6	03-Jul-09	10-Jul-09	0
I130	Hang Doors Lev 2 Seq 12-17	3	13-Jul-09	15-Jul-09	3
I131	Floor Finishes Lev 2 Seq 07-11	6	13-Jul-09	20-Jul-09	0

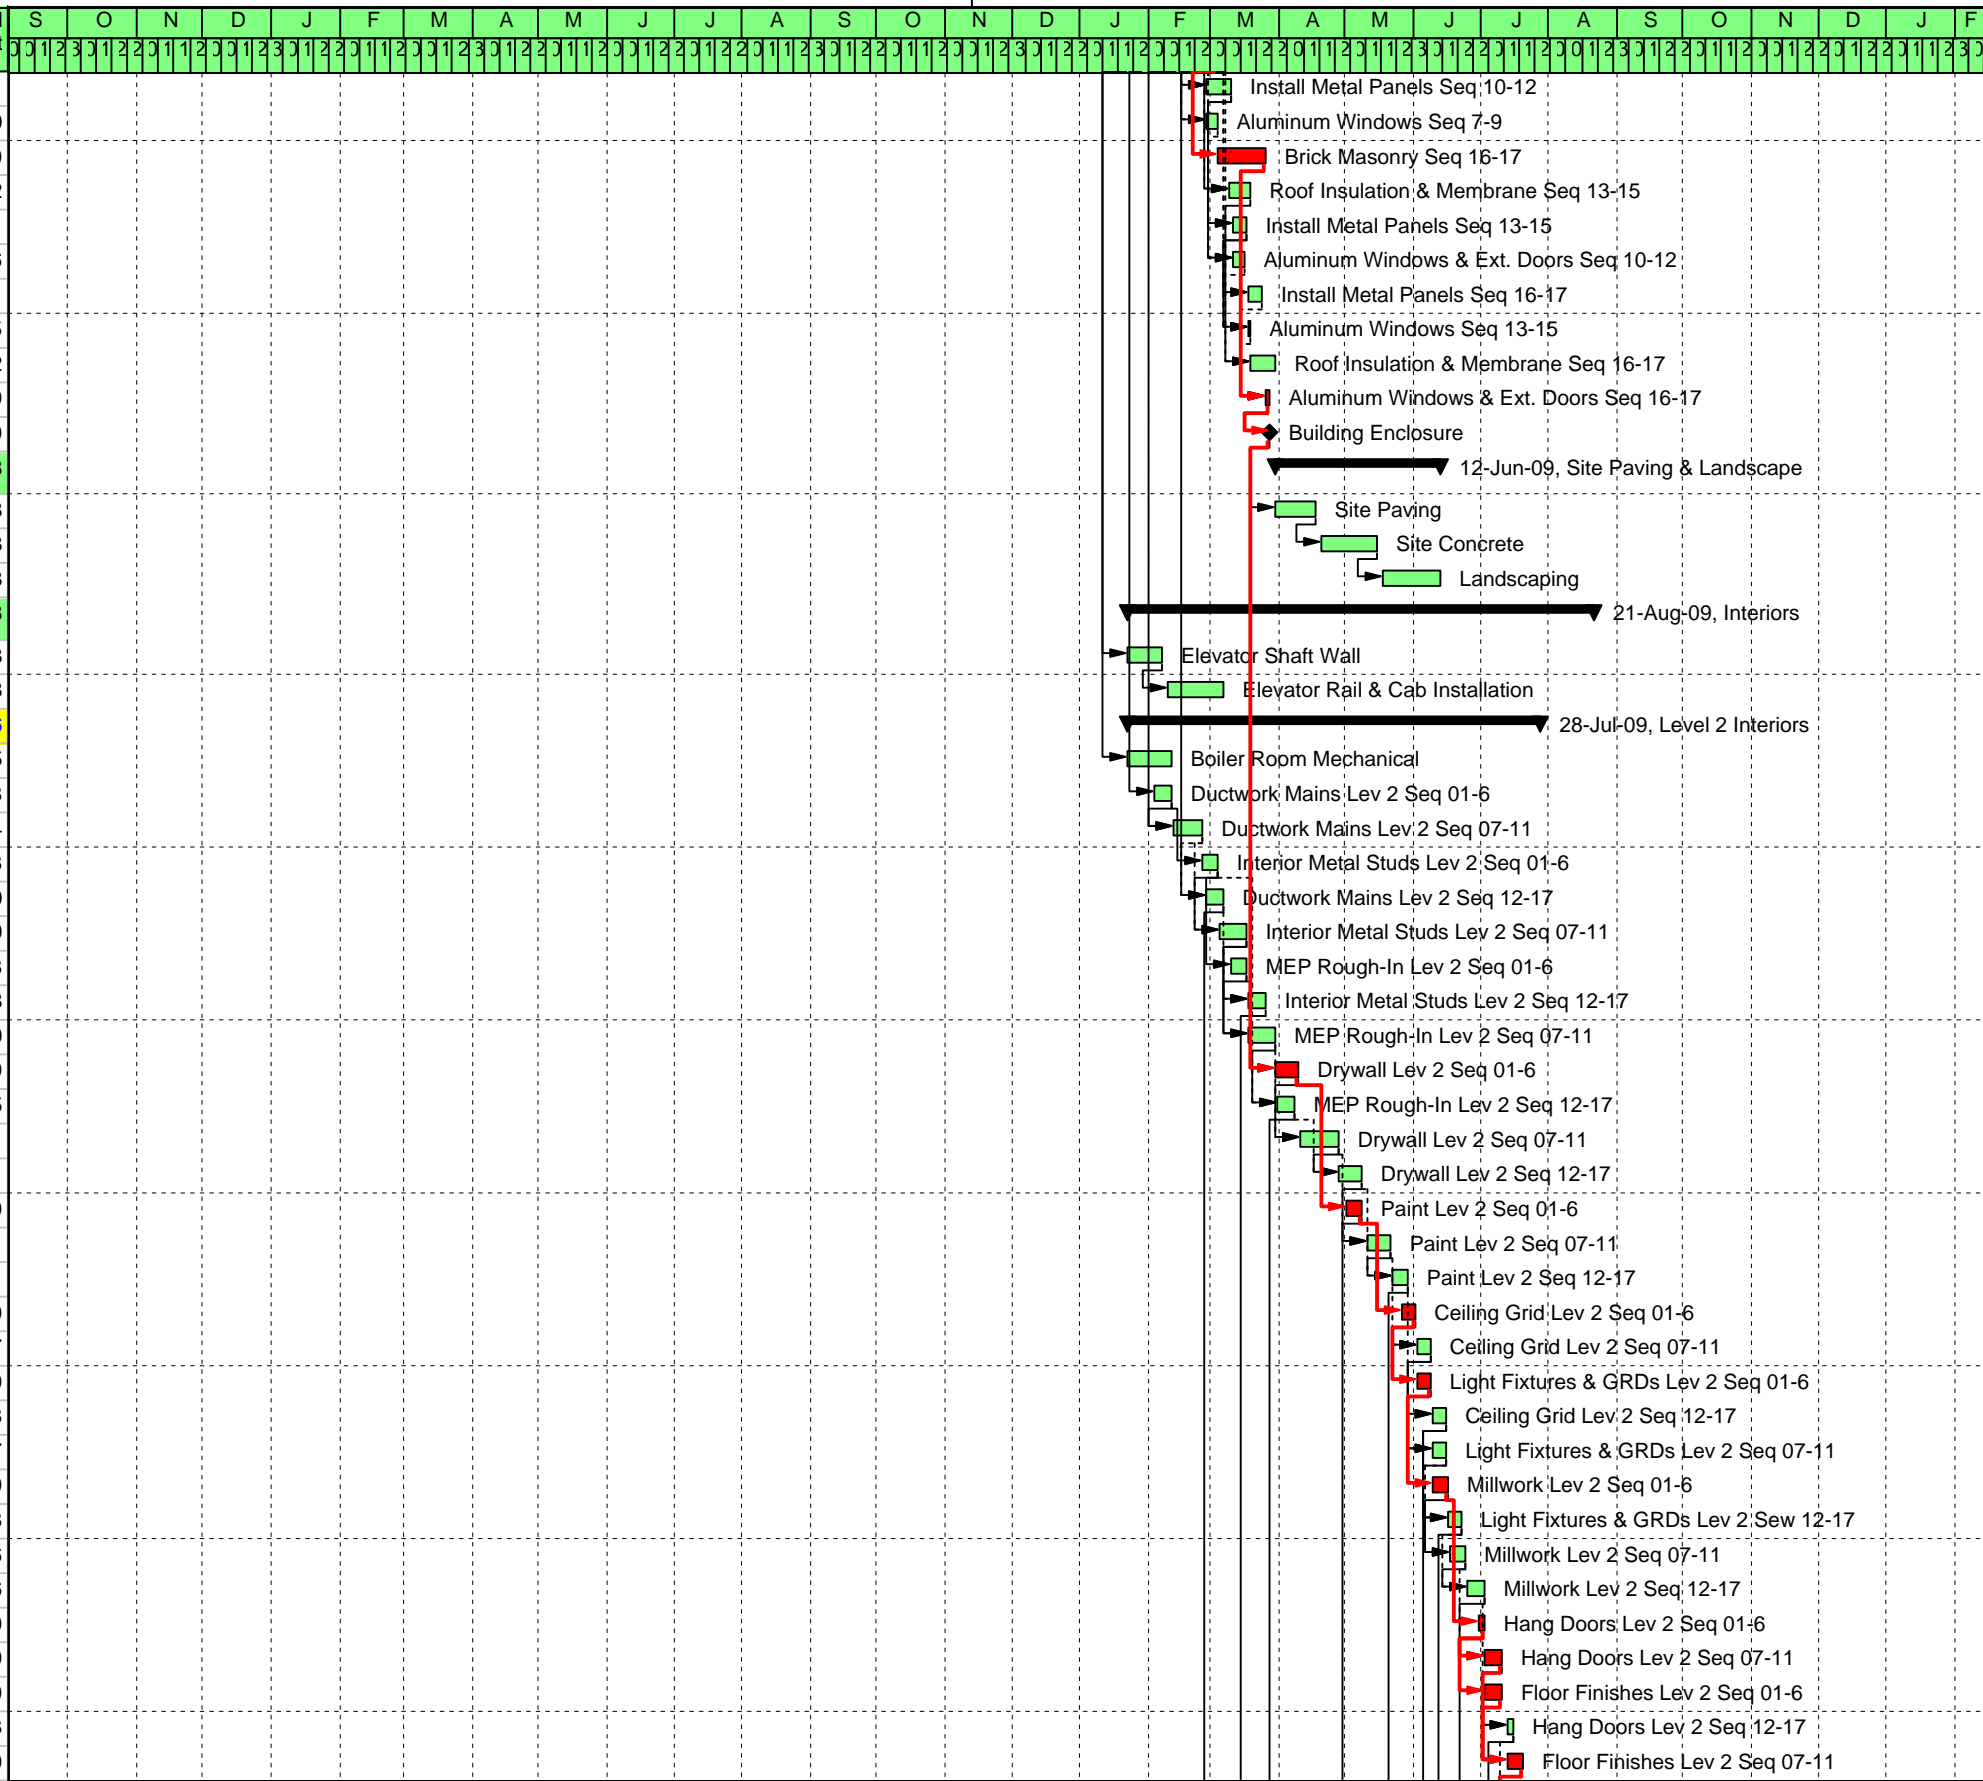

█ Actual Work     █ Critical Remaining Work     ▶ Summary  
█ Remaining Work     ◆ Milestone

