




# The Pennsylvania State University HUB-Robeson Addition and Renovation University Park, PA

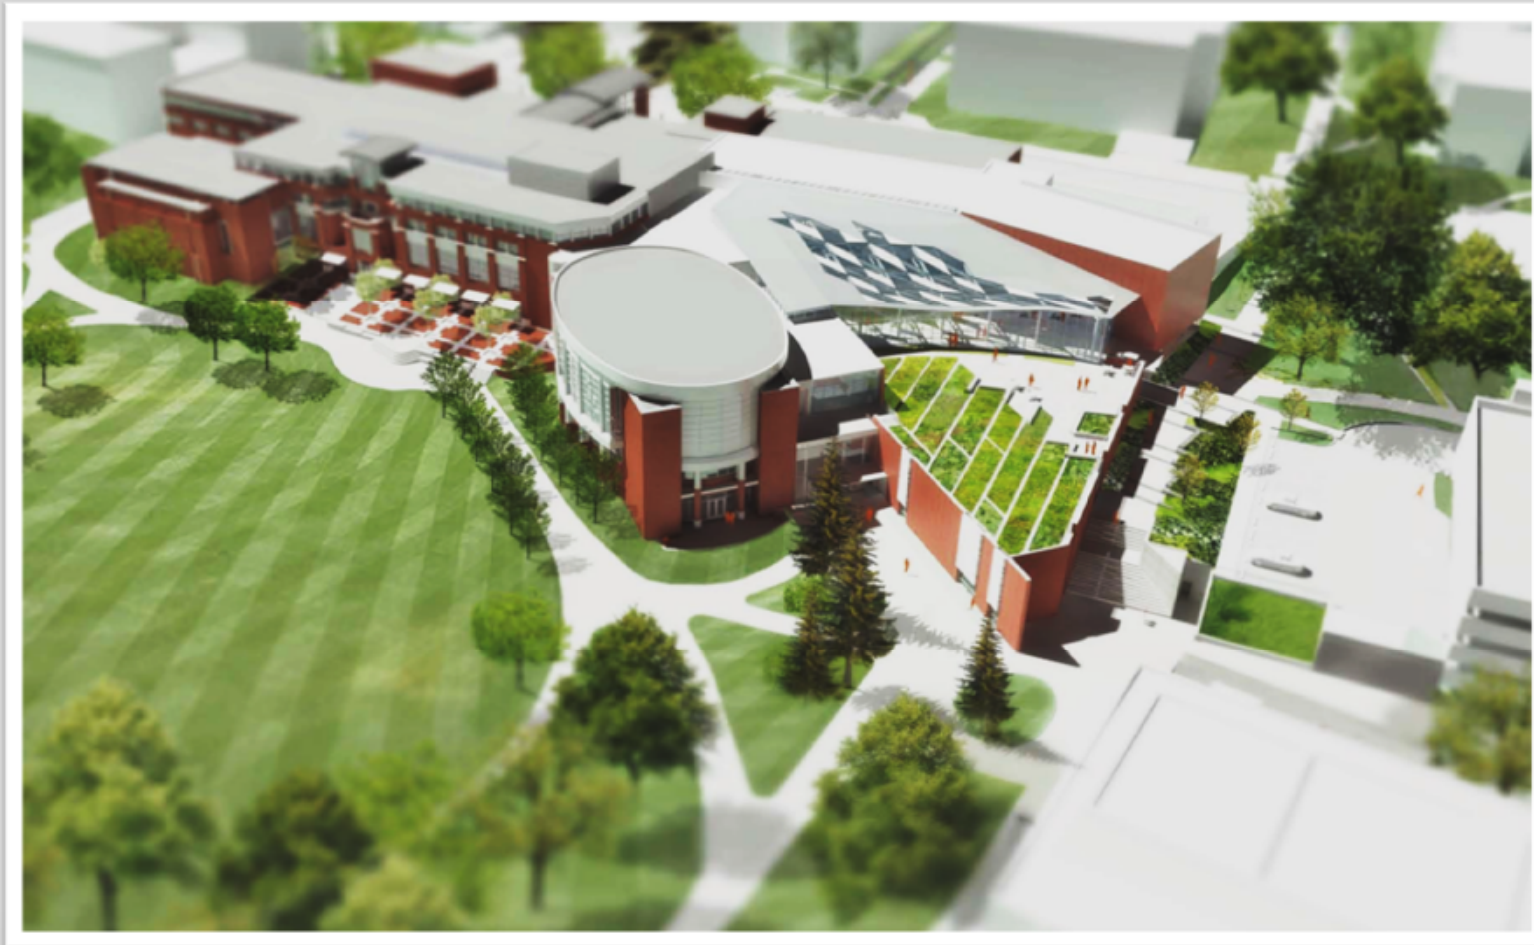

# Work In Progress

- Demolition of Mechanical Systems in the Bookstore
- Demolition in Lower Lobby
- Floor Slab Demolition in Bookstore Sub-Basement for Piles
- Excavate for Pile Caps in Sub-Basement
- Demolition of Towers and Courtyard Facades
- Removal of Soil and Curb near HUB Deck
- Install Bookstore Water Service
- Installation of Revised Emergency Electric Power Conduits

# HUB Parking Deck View



## Top of Parking Deck View



**HUB**  
**EXPANSION**  
FOR THE STUDENTS  
THROUGH COMMUNITY  
COLLABORATION & SAFETY



## South Entrance View



## Loading Dock View



# HUB EXPANSION

FOR THE STUDENTS  
THROUGH COMMUNITY  
COLLABORATION & SAFETY





**HUB**  
**EXPANSION**  
FOR THE STUDENTS  
THROUGH COMMUNITY  
COLLABORATION & SAFETY



**HUB**  
**EXPANSION**  
FOR THE STUDENTS  
THROUGH COMMUNITY  
COLLABORATION & SAFETY



# Planned Work

- Continue Demolition of Towers and Courtyard
- Complete Tower Crane Tower/Opening Demolition
- Continue Demolition in the Bookstore
- Continue Demolition in Lower Lobby
- Complete Removal of Soil and Curb near HUB Deck
- Continue Excavate Pile Caps in Sub-Basement
- Complete Install of Bookstore Water Service
- Continue Grange Building Sitework (pending approval of ramp and grading changes)
