


The Pennsylvania State University HUB-Robeson Addition and Renovation University Park, PA

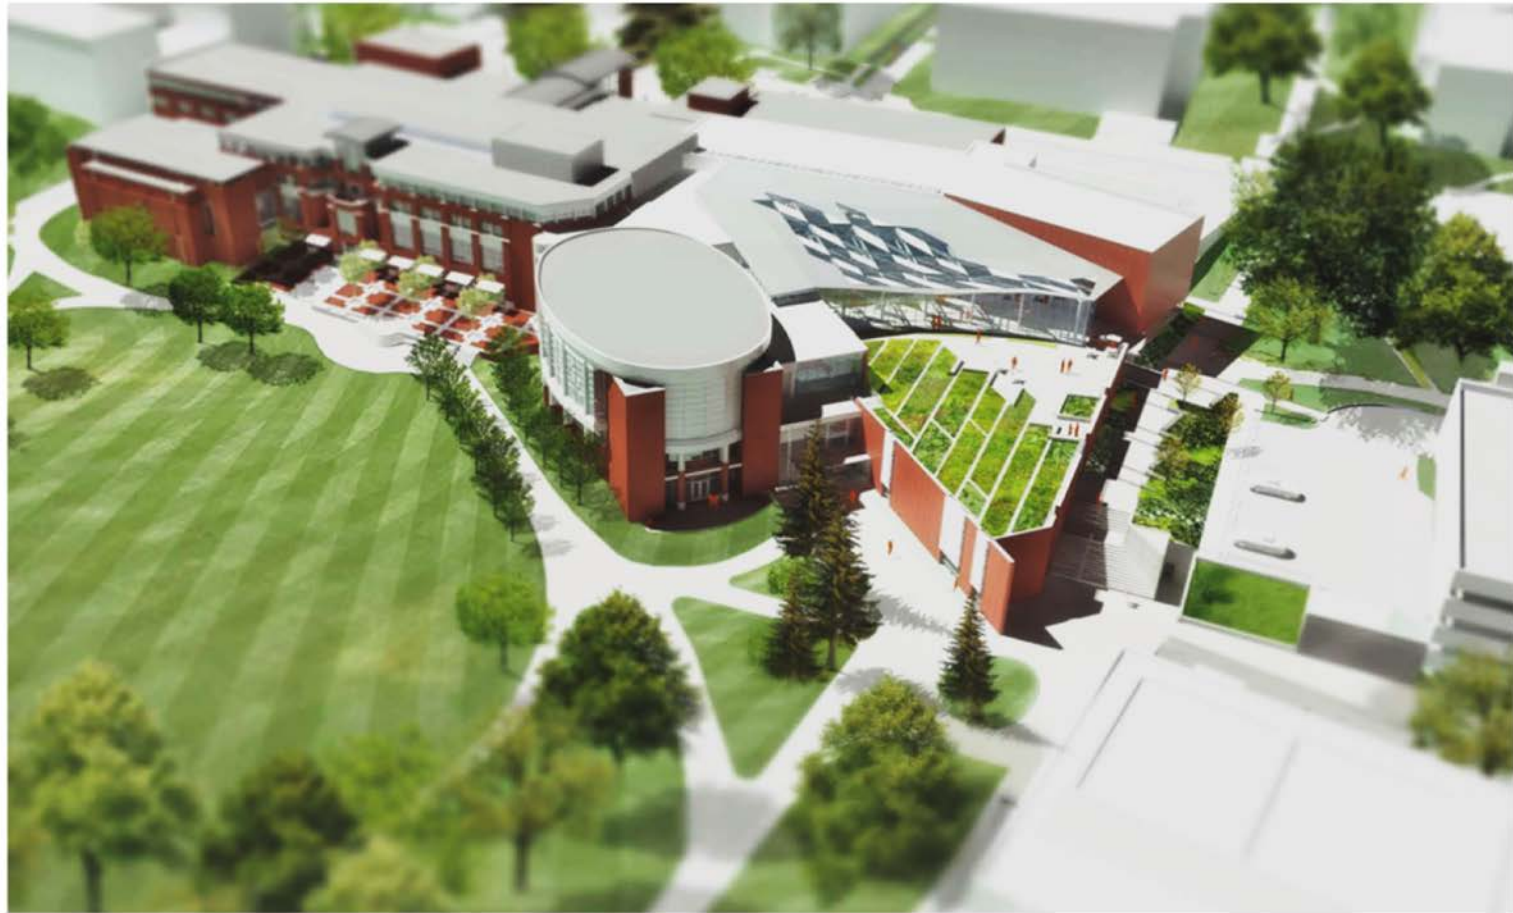

Work In Progress

- Bookstore Mezzanine Steel Erection
- Bookstore Mezzanine Steel Deck Placement
- Excavate Food Service Cooler in Crawlspace
- Excavation in Courtyard
- Demolition of Bookstore Curtainwall
- Demolition of Bookstore Lobby Façade
- Water Protection in 1st Floor Meeting Rooms
- Form and Place Rebar in Courtyard
- Pour Concrete for Courtyard Foundations
- Reinforce Foundation in Bookstore Basement
- Reinforce Elevator Pit in Bookstore Basement
- Relocate Electrical lines in Ceramic Studio Hallway
- Grange Parking Lot Work

Top of Parking Deck View



HUB EXPANSION

FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



HUB Parking Deck View



Loading Dock View



South Entrance View



Courtyard Bulk Excavation



Bookstore Mezzanine Steel



Bookstore Façade Demolition



Meeting Rooms on Level 1 and Mural Protection



Planned Work

- Excavate Food Service Cooler in Crawlspace
- Excavation in Courtyard
- Demolition of Bookstore Lobby Façade
- Relocate Electrical lines in Ceramic Studio Hallway
- Demolition of Bookstore Concrete Mezzanine
- Water Protection in 1st Floor Meeting Rooms
- Form and Reinforce Shear Wall Piers in Food Service Area
- Form and Reinforce Concrete Piers in Bookstore
- Pour Concrete Shear Wall in Courtyard
- Reinforce Foundations and Elevator Pit in Bookstore Basement
- Erect Steel for Bookstore Mezzanine
- Bookstore Mezzanine Steel Deck Placement
- Grange Parking Lot Work
