Lori Farley
Construction Management
10.05.07

VIRGINIA COMMONWEALTH UNIVERSITY

School of Engineering

Project Summary Schedule

ID	Task Name	Duration	Start	Finish
1	**Notice to Proceed**	0 days	Mon 1/16/06	Mon 1/16/06
3	**Sitework**	32 days	Wed 4/5/06	Thu 5/18/06
6	**Cast In Place Concrete**	154 days	Fri 4/14/06	Wed 11/15/06
16	**Water Proofing**	90 days	Mon 5/1/06	Fri 9/1/06
19	**Structural Steel**	75 days	Mon 5/1/06	Fri 8/11/06
22	**Roof Installation**	50 days	Mon 8/21/06	Fri 10/27/06
24	**Fireproof Structural Steel**	26 days	Mon 8/21/06	Mon 9/25/06
26	**Fire Protection**	46 days	Wed 7/26/06	Wed 9/27/06
28	**Masonry/Precast**	123 days	Thu 9/28/06	Mon 3/19/07
32	**SOE SOUTH DRY**	0 days	Thu 10/19/06	Thu 10/19/06
34	**SOE NORTH DRY**	0 days	Fri 10/27/06	Fri 10/27/06
36	**SOE OCTAGON DRY**	0 days	Mon 11/6/06	Mon 11/6/06
38	**Windows and Glazing**	77 days	Fri 12/29/06	Mon 4/16/07
40	**Drywall and Ceilings**	234 days	Fri 8/25/06	Wed 7/18/07
44	**Painting Wall Covering**	52 days	Fri 5/18/07	Mon 7/30/07
46	**Finish Carpentry**	61 days	Fri 6/1/07	Fri 8/24/07
48	**Casework**	55 days	Fri 6/1/07	Thu 8/16/07
50	**Bathroom Tile**	82 days	Thu 4/26/07	Fri 8/17/07
52	**Carpet**	57 days	Fri 6/29/07	Mon 9/17/07
54	**Terazzo**	53 days	Fri 9/7/07	Tue 11/20/07
56	**Mechanical and Plumbing**	300 days	Wed 7/26/06	Tue 9/18/07
58	**Test & Balance HVAC**	16 days	Tue 8/28/07	Tue 9/18/07
61	**Electrical**	347 days	Fri 4/28/06	Mon 8/27/07
63	**Elevators**	49 days	Thu 8/24/06	Tue 10/31/06
66	**Final Hardscape & Paving**	46 days	Mon 4/16/07	Mon 6/18/07
69	**Final Landscaping**	30 days	Thu 7/12/07	Wed 8/22/07
71	**Owner FFE**	44 days	Fri 9/28/07	Wed 11/28/07
73	**Substantial Completion**	0 days	Wed 11/28/07	Wed 11/28/07
75	**Spring Semester Begins**	0 days	Mon 1/14/08	Mon 1/14/08

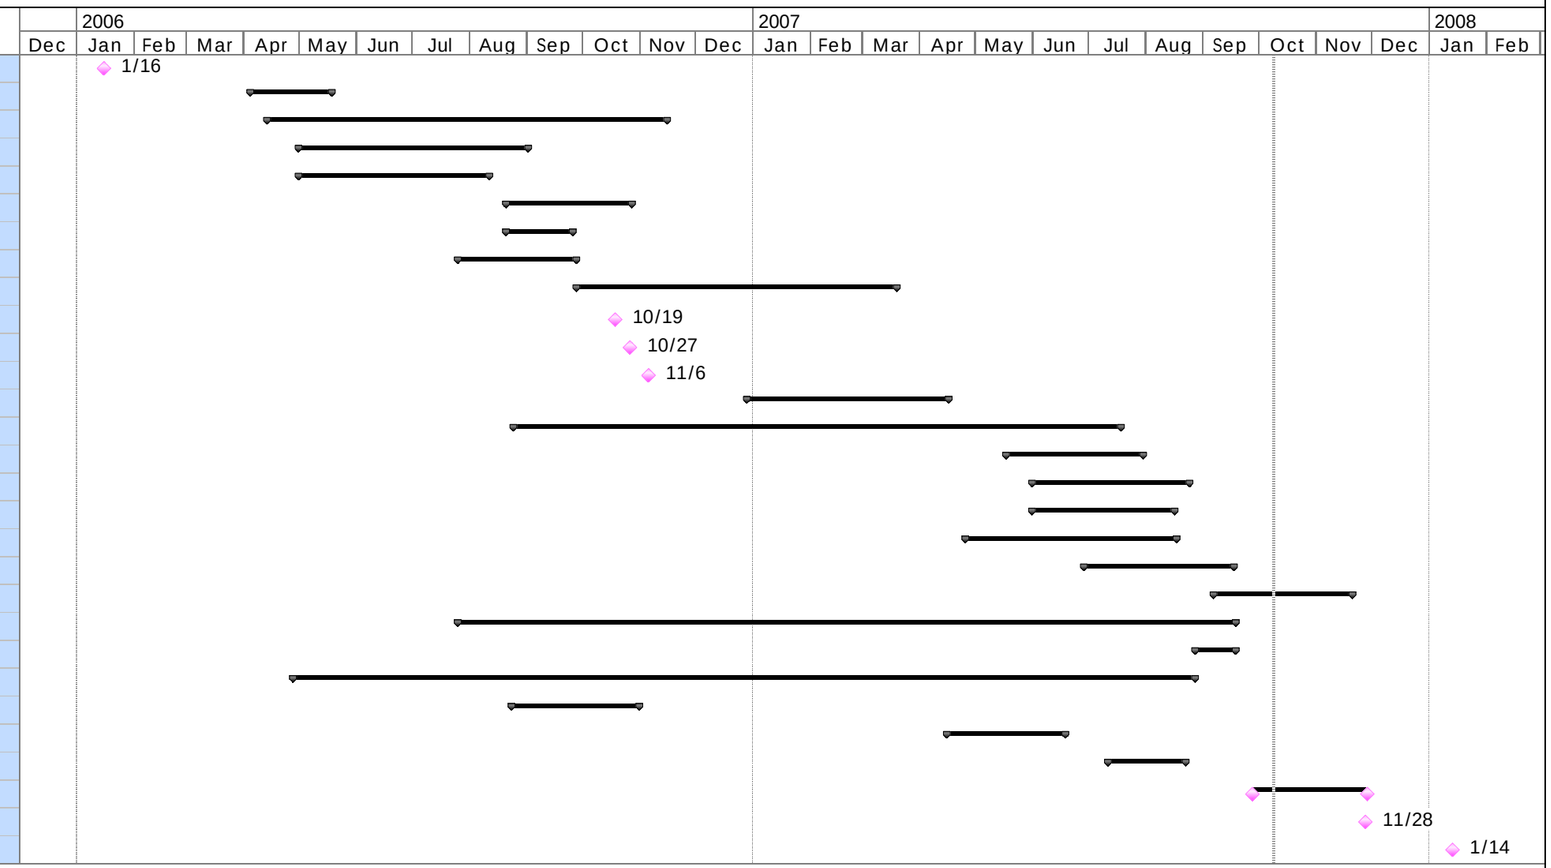

Project: SOE SCHEDULE
Date: Tue 10/9/07

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
